





Islamic Republic of Afghanistan
Ministry of Finance
Ministry of Public Works
Ministry of Rural Rehabilitation
& Development



**National Rural Access
Program
(NRAP)**

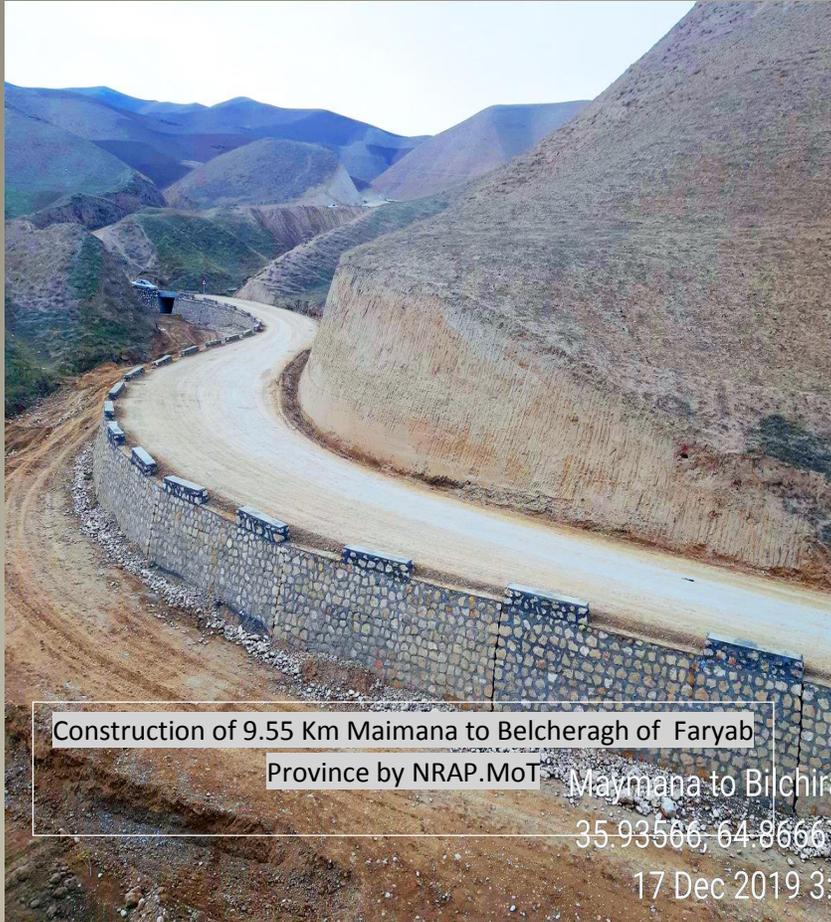

Construction of 9.55 Km Maimana to Belcheragh of Faryab Province by NRAP.MoT
Maymana to Bilchira
35.93566, 64.86667
17 Dec 2019 3:

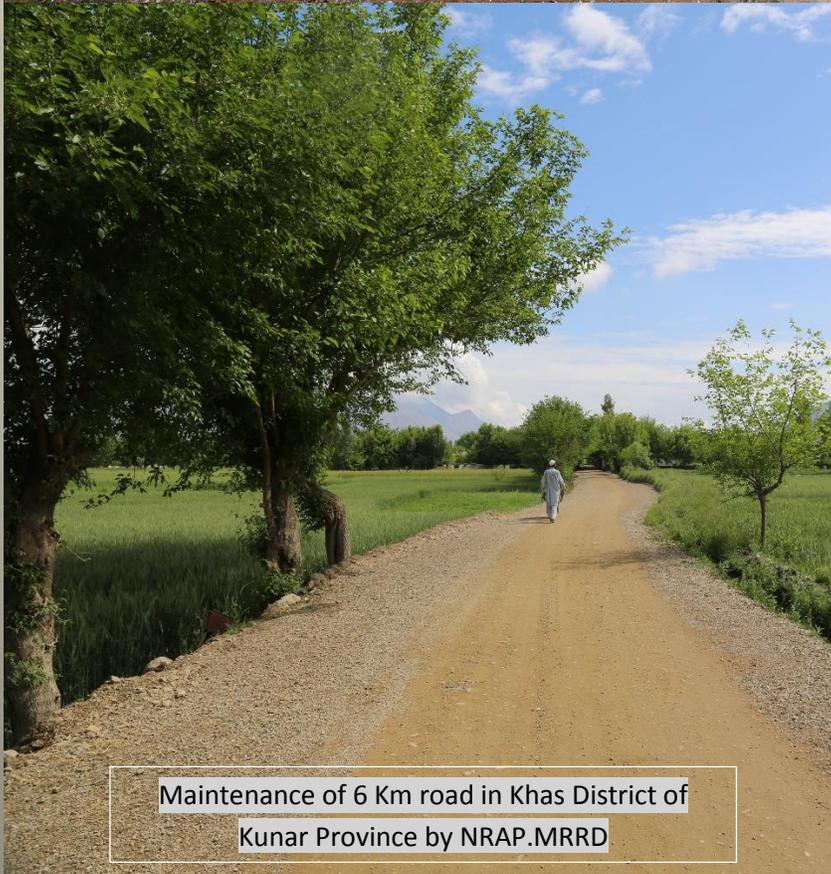

Maintenance of 6 Km road in Khas District of Kunar Province by NRAP.MRRD

Note:

NRAP got high capacity to deliver quality and high standard roads while insecurity and cold winter remained robust threat for implementation during the quarter.

4th Quarter Report 1398

(21 December, 2019 – 20 March, 2020)


Prepared by:

Besmillah Besmil/Daryosh Tabesh

ROAD NETWORK & PLANNING SURVEY WORK PROGRESS REPORT



AFGHANISTAN Map

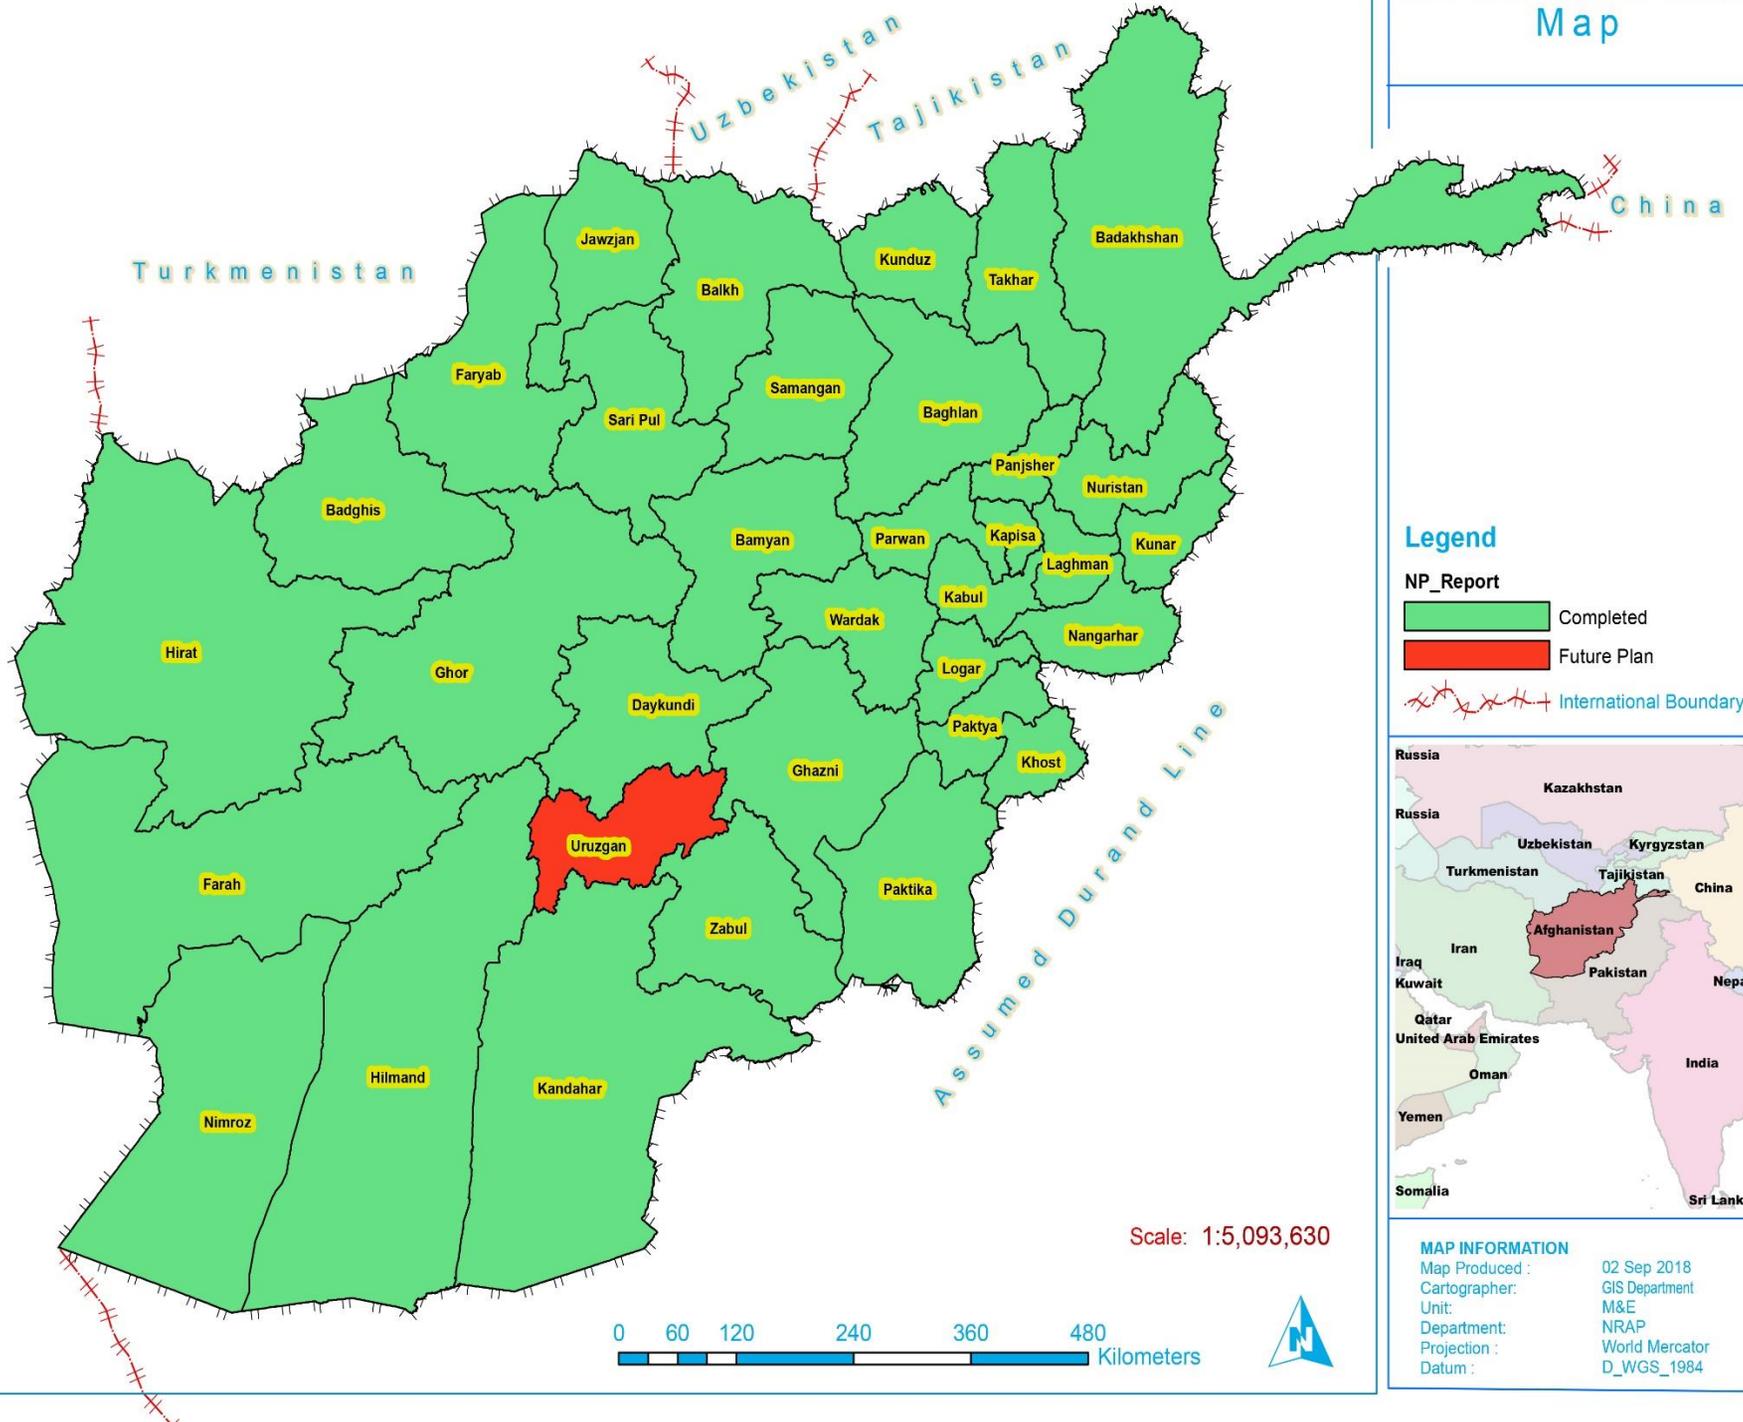

Legend

NP_Report

- Completed
- Future Plan
- International Boundary



Scale: 1:5,093,630



MAP INFORMATION

Map Produced : 02 Sep 2018
 Cartographer: GIS Department
 Unit: M&E
 Department: NRAP
 Projection : World Mercator
 Datum : D_WGS_1984

Table of Contents

ABBREVIATIONS AND ACRONYMS:	e
EXECUTIVE SUMMARY	1
1) COMPONENT (A) SECONDARY ROADS-MOT	1
2) COMPONENT (B) TERTIARY ROADS-MRRD	1
3) COMPONENT (C) PROGRAM PLANNING & DEVELOPMENT, INSTITUTIONAL STRENGTHENING, AND PROGRAM COORDINATION SUPPORT	1
AFGHANISTAN RURAL ACCESS PROJECT (ARAP).....	3
I. PHYSICAL PROGRESS	3
1. COMPONENT (A) DISTRICT ROADS	3
2. COMPONENT (B) VILLAGE ROADS	5
3. COMPONENT (C) PROGRAM PLANNING & DEVELOPMENT, INSTITUTIONAL STRENGTHENING, AND PROGRAM COORDINATION SUPPORT	7
II. FINANCIAL PROGRESS	8
OTHER ONGOING PROJECTS UNDER (NRAP).....	10
1. NRAP-MoF	10
3. JICA & GOA Fund	10
CHALLENGES AND OBSTACLE	11
1. INSECURITY	11
2. MATERIAL COST	11
3. CAPACITY OF PRIVATE SECTOR	11
ANNEXES (A) MoT	i
ANNEX (B) MRRD:	vi

Abbreviations and Acronyms:

APRP	Afghanistan Peace and Reintegration Project
ARAP	Afghanistan Rural Access Project
ARTF	Afghanistan Reconstruction Trust Fund
AUSAID	Australian Agency for International Development
CARD-F	Comprehensive Agriculture and Rural Development Facility
CHL	Central Highlands
CIDA	Canadian International Development Agency
DLP	Defect Liability Period
EM	Emergency Maintenance
ESM	Environmental and Social Monitoring
ESMF	Environmental and Social Safeguard Framework
FA	Financial Audit
GOI	Government of India
GOV	Government
GRC	Grievance Redress Committees
IDA	International Development Association
JF	Japan Fund
JICA	Japan International Cooperation Agency
Km	Kilometer
M	Meter
MIS	Management Information System
MoF	Ministry of Finance
MoT	Ministry of Transport
MoPW	Ministry of Public Works
MRRD	Ministry of Rural Rehabilitation and Development
NCU	National Coordination Unit
NEEP	National Emergency Employment Program
NEEPRA	National Emergency Employment program for Rural Access
NERAP	National Emergency Rural Access Project
NPP	National Priority Program
NRAP	National Rural Access Project
PAP	Project Affected Person/People
PDO	Project Development Objectives
PIU	Program Implementation Unit
PRI	Project Result Indicators
QA/QC	Quality Assurance & Quality Control
RCC	Reinforced Cement Concrete
RM	Running Meter
SCM	Steering Committee Meeting
SIDA	Swedish International Development Cooperation Agency
SMM	Senior Management Meeting
SMT	Senior Management Team
TA	Technical Audit
URAP	Uruzgan Rural Access Project
USAID	United States Agency for International Development
WB	World Bank

EXECUTIVE SUMMARY

This summary consolidates the overall progress made during 4th quarter of 1398 toward performance indicators of all projects including ARAP. The highlights include the achievements of components A, B, C and D of the mega project ARAP while briefly indicated a general progress of other projects under NRAP during the reporting period. Annexes (A) & (B) explains the required details.

- 1) COMPONENT (A) SECONDARY ROADS-MoT:** The PIU_MoT remains responsible for construction, rehabilitation and maintenance of major local roads (district roads) under component A, during the project life. This component has succeeded to construct and rehabilitate 782.17 Km gravel surfaced road, 263.67 Km asphalt surfaced road and 1,489.1 Running meters of bridges as well as constructed 135,672 linear meter associated drainage structures, which generated 5,578,808 labor days to communities' in subproject vicinity since inception to date. While, 26.09 Km gravel surface road is constructed during the reporting period.
- 2) COMPONENT (B) TERTIARY ROADS-MRRD:** PIU-MRRD is the executing authority of this component and it is responsible to improve, construct and maintain minor local roads (village roads). The cumulative physical achievement since inception; 2012 of the project to the end of 4th quarter of 1398 is construction of 1,539 Km of village roads, 2,442 Running meter bridge (includes 514 Rm bridges under B1), 90,614.17 linear meters associated drainage structures as well as generated 5,104,244 labor days. Whereas indicative rehabilitation of 10 Km road is reported during the reporting period.
- 3) COMPONENT (C) PROGRAM PLANNING & DEVELOPMENT, INSTITUTIONAL STRENGTHENING, AND PROGRAM COORDINATION SUPPORT:** This component is jointly executed by MoT and MRRD for various activities which will be undertaken by each individual, while ensuring close coordination with each other, facilitated by the National Coordination Unit (NCU).
 1. Gap Analysis in national road network including district road has been conducted. New version of road network database has been released and data collection of road network planning is completed for 33 provinces, 85% of national highways.
 2. Since inception of the project different types of short, long term and on the job trainings were provided to individuals, meeting the preset selection criteria. Both domestic and international trainings provided to program staff in different fields such as, CCNA, MSCD, Project Management and Academic English courses to civil servant, while required on job trainings were provided to internship students and fresh graduate engineers indoor. Moreover, it is worthy to report that constructions of all 8 NRAP buildings are completed.
 3. Beside regular data flow to program stakeholders through NRAP website, newsletter, media report; steering committee meetings, monthly coordination meeting, technical coordination meeting as well as ad hoc Senior Management Meeting conducted for project preparation and other related issues.
- 4) COMPONENT (D) CONTINGENCY EMERGENCY RESPONSE:** This component with allocated US\$ 0 budget is for contingency and emergency response that will allow for rapid response in the event of an adverse natural or man-made event that causes a major disaster through the reallocation of project fund. There is no achievement under this this component yet.

ARAP Project Physical Progress Status As of March 2020

Intermediate Result Indicator	Unit	*PRI	5th Year Indicator	Achievements	Progress as per PRI (%)	Progresses per 5th year indicator(%)	Variance + -%
Financial management system in MRRD and MPW developed and functional	%	100	100	100.00		100.00	0.00
Cost estimation system developed and fully functional	%	100	100	100.00		100.00	0.00
Design Standards developed and adopted	%	100	100	90.00		90.00	-10.00
Improved network Management System in Place	%	100	100	100.00		100.00	0.00
Complete Road Inventory (100% of roads under central government mandates, Including major highways, secondary roads and tertiary roads under NRAP sponsorship)	%	100	100	85 % major highways and secondary roads	85.00	85.00	-15.00
				0 % tertiary roads	0.00	0.00	-100.00
Roads constructed, Rural	Km	2670	2550	2584.85	96.81	101.37	1.37% ahead
Km of gravel surfaced secondary roads rehabilitated	Km	1000	1000	782.17	78.22	78.22	The performance has been expedited to achieve the set indicators
Km of asphalt surfaced secondary roads rehabilitated	Km	250	250	263.68	105.47	105.47	5.47% ahead
Construction of bridges on secondary roads	Meter	1000	1000	1489.10	148.91	148.91	48.91% ahead
Km of secondary roads under routine and periodic maintenance scheme	Km	1000	1000	2178.03	217.80	217.80	117.80% ahead
Km tertiary roads rehabilitated	Km	1420	1300	1539.00	108.38	118.38	18.38% ahead
Construction of bridges on tertiary roads	Meter	1600	1600	1928.00	120.50	120.50	20.50 ahead
Km of tertiary roads under routine and periodic maintenance scheme	Km	2000	2000	5731.00	286.55	286.55	186.55 ahead
Job opportunities created via the intervention	Million Labor days	11.92	-	10.68	89.62	-	-10.38
Number of People trained or retrained	# people annually	-	833	91.00		10.92	-89.08
Female: Number of people trained or retrained (20% of total number of people)	# Female annually	-	167	30.00		17.96	-82.04

*PRI- Project Result Indicator

AFGHANISTAN RURAL ACCESS PROJECT (ARAP)

I. PHYSICAL PROGRESS

1. COMPONENT (A) DISTRICT ROADS

Subcomponent A1, A2 & A3: By completion of fourth quarter of 1398, component A has successfully completed rehabilitation of 782.17 Km of gravel surface, 263.67 Km asphalt surface road and constructed 1,489.1 Rm of bridges through total 130 contracts since inception of the project. While total 11 contracts for rehabilitation of total 116.25 Km road ((90.27 Km gravel roads, 26.31 Km asphalt roads) is positively in progress.

Bellow table indicates the details progress since inception and during the reporting quarter.

Activities	Surveyed			Designed			Awarded			Completed		
	Previous	This Quarter	Total	Previous	This Quarter	Total	Previous	This Quarter	Total	Previous	This Quarter	Total
Rehabilitation of secondary Road (1000 KM) gravel	1037.71	0	1037.71	1037.71	0	1037.71	956.64	0	956.64	756.08	26.09	782.17*
Construction Bridge (1000 RM) over secondary road	1,480.1	0	1,480.1	1,480.1	0	1,480.1	1,480.1	0	1,480.1	1,489.1	0	1,489.1**
Upgrading of 250Km secondary road to asphalt surface	400.10	0	400.10	400.10	0	400.10	314.52	0	314.52	263.67	0	263.67

*782.17 Km road includes, 701.82 Km road of Completed sub-projects, 32 Km road post disaster sub-project that meets the criteria of gravel surfaced roads and 48.35 Km accessibility achieved in cancelled sub-projects.

** 1480.1 Rm bridges awarded initially but after applying variation to one of the sub-projects now actual construction lengths changed to 1489.1 Rm of bridges.


Subcomponent A4: This subcomponent allocated for maintenance of secondary road. The periodic maintenance applied to 671.03 Km road and 34 emergency maintenance contracts completed since inception of the project to the end of 4th quarter of 1398. Likewise, 507 contracts with total length of 1,507 Km road (it has been contracted for four & five rounds that cumulatively total 5537 Km length of roads are covered under routine maintenance) is completed under routine maintenance.

Furthermore, 9 post disaster sub-projects with total cost of 2,485,508.35\$ and generation of 263,671.01 labor days are successfully completed since inception of the project under this sub component.


Labor Days Generated

Descriptions	Since Inception	This Quarter
Labor days generated	5,578,808	44,862

Subcomponent A5: ESM report for 4th Quarter of 1398, no ESM Plans are prepared during the reporting period, 316 beneficiaries (204 males and 112 female) were trained/consulted, 14 community consultations meetings (10 with male and 4 with female) held at different stages of the projects. Likewise, 2 grievance redress committee (0 Male GRC and 2 Female GRC) has established, 10 subprojects visited and 6 different issues such as air pollution, hiring more community laborers by contractor, design and land donation were raised by the communities and most of the issues solved through consultation with contractors and providing technical information to communities during the reporting period.

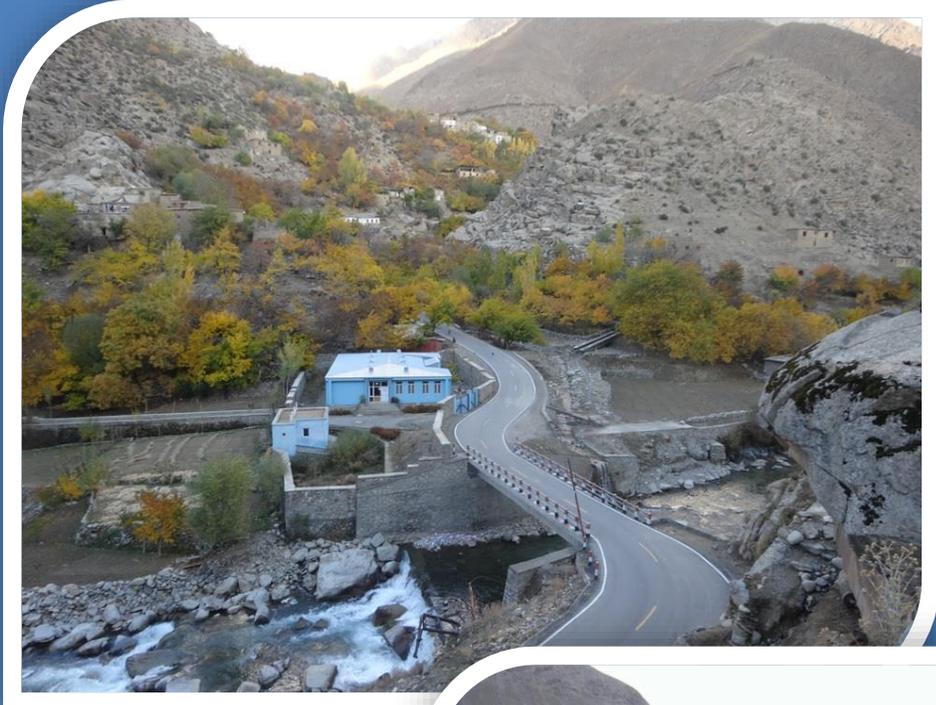

Construction of 3.7 Km Poojawa road in Pamjshir Province By NRAP.MoT

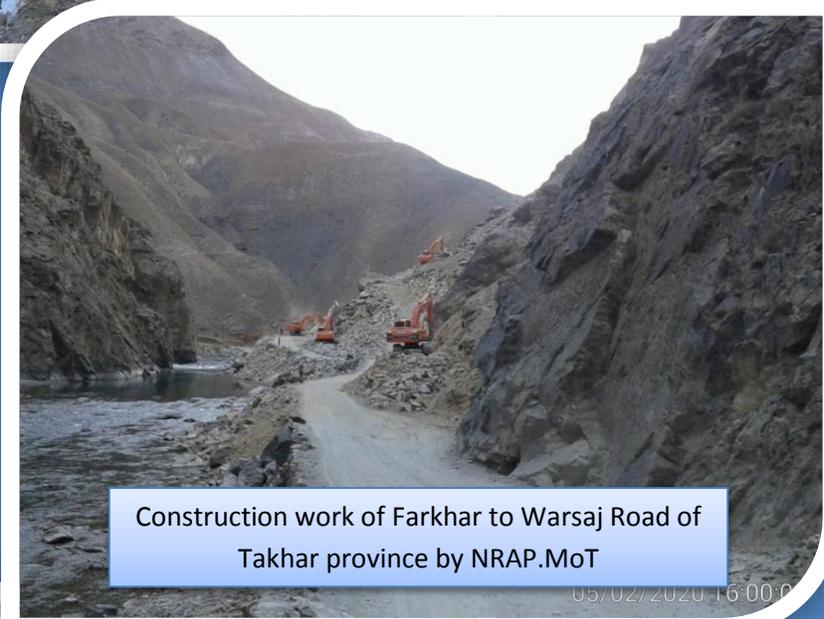

Construction work of Farkhar to Warsaj Road of Takhar province by NRAP.MoT

05/02/2020 16:00:00



Gender Workshop Conducted by NRAP.MoT

1. COMPONENT (B) VILLAGE ROADS

Subcomponent B1 & B2: These sub-components of ARAP has successfully rehabilitated indicatively 10 km of roads and generated 15,593 labor days during reporting period. While total 1,539 Km of roads, 2,442 running meters of bridge and 90614.17 linear meter associated drainage structures have been constructed since inception of the project. Moreover, 42 contracts to rehabilitated 63.15 Km of roads and 30 running meters of bridge is ongoing.

Bellow table indicates the details progress since inception and during the reporting quarter.

Activities	Surveyed			Designed			Awarded			Completed		
	Previous	This Quarter	Total	Previous	This Quarter	Total	Previous	This Quarter	Total	Previous	This Quarter	Total
Rehabilitation of tertiary Road (1300 KM) gravel	1696	0	1696	1,680	0	1,680	1,623	0	1,623	1,529	10	1,539*
Construction Bridge (1600 RM) over secondary road	3,311	0	3,311	2,756	0	2,756	2,527	0	2,527	2,442	0	2,442**

*indicatively

**including 514 Rm completed under B1.

Subcomponent B3: This subcomponent is maintenance centric and entails emergency, routine and periodic maintenance of ARAP constructed village road.

Emergency Maintenance: emergency repairing of flood affected roads and road structures executed through this sub-component. Community execute the contracted work in vulnerable segments of road network. Sixty-Eight emergency contracts have signed for repairing and maintenance of infrastructures as well as clearing of road surfaces due to flood and landslides under this subcomponent since inception of the project.

Snow Cleaning: As of 4th quarter of 1398 almost 758 km of tertiary roads has been unblocked through 81 contracts under this subcomponent in all over the country. NRAP/MRRD toke immediate action with a specific plan for cleaning the affected tertiary roads.

Routine Maintenance: This subcomponent incorporate routine maintenance of the program constructed village roads. So far 3,600 km of tertiary road kept functional under routine maintenance since inception of the project and as of now no routine maintenance is ongoing for tertiary roads in ARAP project.

Periodic Maintenance: Periodic maintenance constitutes part of the Component B3. Insofar, 199 contracts include 2,156 km road have been completed under this subcomponent of ARAP project.

Moreover, 63 contracts include 565 km road is completed under periodic maintenance through MoF project.

Labor Days Generated

Descriptions	Since Inception	This Quarter
Labor days generated	5,104,244	15,593

Subcomponent B4: During the 4th quarter of 1398, total 14 ESMP were prepared, 2,305 (2,175 M, 130 F) people were trained, 41 coordination meetings have been held, 48 GRC (32 M, 16 F) have been established. Likewise, 28 Community Participatory Monitoring and 0 social audit have been conducted, 3 social issues such as land acquisition have been solved and 25 environmental monitoring have been conducted. Finally yet importantly 1,459 m2 of lands donated by the communities during the reporting period.



Construction of 30 Rm Bridge in Khost
District of Baghlan Province By NRAP.MRRD



Construction work of 17 km road in Guzara District
of Hirat Province by NRAP.MRRD



NRAP ISM Meeting

3 COMPONENT (C) PROGRAM PLANNING & DEVELOPMENT, INSTITUTIONAL STRENGTHENING, AND PROGRAM COORDINATION SUPPORT

The overall objective of this component is institutional strengthening, project management and program development which are segregated into three subcomponents of C1, and C2 and C3. The subcomponents are articulated as below:

Subcomponent C1 (Rural Roads Network Planning and Management System): A joint technical meeting conducted between both PIUs to evaluate the technical aspects of the Network Planning and Management System.

Moreover, NRAP/MoT has the responsibility of data collection for primary and secondary road network. The data collection has been successfully completed in 18,876.39 Km in which 85% of national highways, 33 provinces except Uruzgan due to high security risk and also social surveys conducted in 12,340 social centers as end of 4th quarter of 1398.

Besides, under this subcomponent an assignment was given by the World Bank delegates to NRAP team in order to prioritize 1000 Km of secondary roads using the collected data. The assigned team (GIS, planning and economic analysis teams of both PIUs led by Mr. Maiwand Hoshmand and Mr. Mansoor Mansoori) has reported that they have analyzed 18,876.39 Km of roads including District roads, Provincial roads and National Highways, taking into consideration the indicator of poor, fair and good using the condition survey data. After comprehensive data analysis and clean up as a result they summarized the outcome as follow:

- Out of surveyed roads, 60% roads are unpaved and 40% roads are paved.
- Out of surveyed roads, 56% is district roads, 36% National Highways and 7% is provincial roads.
- Out of surveyed roads, 22.63% of roads are in good condition, 39.27% of roads are in fair condition and 38.07% roads are in poor condition.

As a resulted 902 Km of secondary road has been selected to survey and design department of PIU-MoT.

Subcomponent C2 (Institutional Strengthening and Capacity Building): Throughout the reporting period different types of short-term trainings are provided for NRAP staff inside and outside the country. Following is some of in progress trainings for NRAP staff during 4th quarter of 1398:

- Master degree programs for NRAP staff are under process.
- Post- Graduation course for NRAP staff under process.
- HDM4 training for road network prioritization is conducted at Kazakhstan for both PIUs and NCU technical Staff.
- Planning of a study tour is ongoing for program staff.

Furthermore, as one of the activities under this subcomponent is construction of functional office and laboratory buildings in the eighth regional offices and improving the program library, so construction works of all 8 NRAP buildings is completed since inception of the project.

Total Training Conducted during 1398

<i>Descriptions</i>	<i>Year 1398</i>	<i>This Quarter</i>
Male Trainee	61	0
Female Trainee	30	0
Total Trainee	91	0

Subcomponent C3 (Program Coordination Support): Regular data flow to the program stakeholders through NRAP website, publishing monthly newsletter, media reporting, steering committee meetings, monthly coordination meeting, technical coordination meeting as well as ad hoc Senior Management Meeting for the project preparation and other related issues are commencing under this subcomponent.

Following is some completed activities under this subcomponent during the reporting period:


- publishing and distribution of monthly newsletter
- Timely media reporting
- One monthly coordination meeting is conducted.
- Quarterly Financial Report (IUFRR) prepared and distributed.
- ISM World Bank supervisory meeting is conducted.
- Two Senior Management team meeting is conducted

4 **COMPONENT (D) CONTINGENCY EMERGENCY RESPONSE:** This component will allow for rapid response in the event of an adverse natural or man-made event that causes a major disaster through the reallocation of project fund. It could also be used to channel additional funds for emergency response should they become available.

II. FINANCIAL PROGRESS

Component wise cumulative and Quarterly Financial Progress till 31 st March 2020				
Components	Total Project Budget (US\$ m)	Expenditures for this Quarter (US\$ m)	Cumulative Expenditures (US\$ m)	Balance(US\$ m)
Sub-total of Component A	\$268.00	\$1.22	\$218.57	\$49.43
Sub-total of Component B	\$143.00	\$1.17	\$146.83	(\$3.83)
Sub-total of Component C	\$26.00	\$0.04	\$7.62	\$18.38 **
Grand Total	\$437.00	\$2.43	\$373.03	\$63.97


** US\$3m SDR loss include

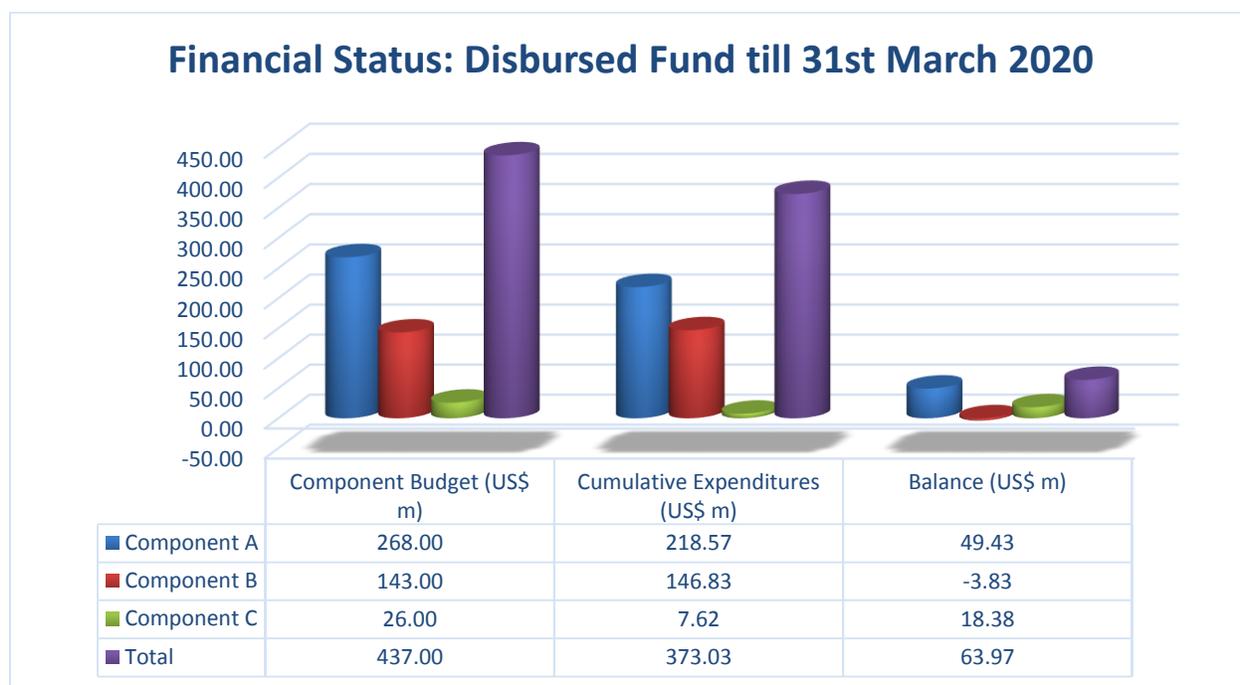

Financial Vs Physical Progress of Major Activities of Component A					
Component Major Activities	Allocated Budget (US\$)	Disbursement Amount (US\$)	Financial Progress %	Physical Progress as per 5th year indicator (%)	Balance (US\$)
Gravel Surfacing	\$110,440,000	\$79,811,449.50	72.27	78.22	\$30,628,550.50
Asphalt Surfacing	\$76,590,000	\$60,449,177.53	78.93	105.47	\$16,140,822.47
Bridge construction	\$15,470,000	\$13,883,920.99	89.75	148.91	\$1,586,079.01
Road maintenance	\$21,000,000	\$19,491,556.12	92.82	217.80	\$1,508,443.88
Implementation support	\$44,500,000	\$44,938,587.71	100.99	-	-\$438,587.71

Financial Vs Physical Progress of Major Activities of Component B					
Component Major Activities	Allocated Budget (US\$)	Disbursement Amount (US\$)	Financial Progress %	Physical Progress as per 5th year indicator (%)	Balance (US\$)
Gravel Surfacing	\$70,500,000	\$76,991,178	109.21	118.38	-\$6,491,178.13
Bridge construction	\$13,000,000	\$11,931,372	91.78	120.50	\$1,068,628.39
Road maintenance	\$25,500,000	\$23,369,092	91.64	286.55	\$2,130,907.94
Implementation support	\$34,000,000	\$34,541,821	101.59	-	-\$541,820.86

Component Wise Fund Commitment Status			
Components	Component Budget (US\$ m)	Disbursed Budget (US\$ m)	Committed & Allocated (US\$ m)
Component A	\$268,000,000	\$218,574,692	\$49,425,308
Component B	\$143,000,000	\$146,833,463	(\$3,833,463)
Component C	\$26,000,000	\$7,622,728	\$18,377,272
Grand Total	\$437,000,000	\$373,030,883	\$63,969,117

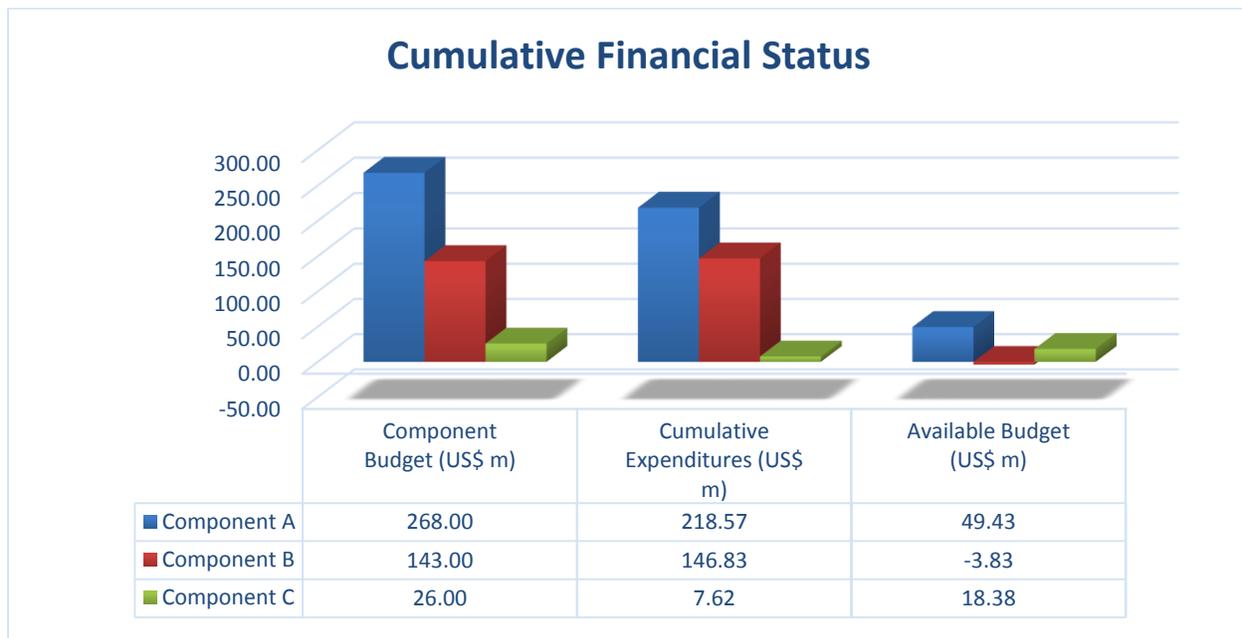

OTHER ONGOING PROJECTS UNDER (NRAP)

1. NRAP-MoF

This project funded by the Islamic Republic of Afghanistan through Ministry of Finance with cumulative budget of US\$166.4 million in different years.

NRAP/MRRD has succeeded to complete 492 contracts under this project and achieved construction of 1,719 km of roads, 3,299 running meters of bridge and it has generated 2,323,466 labor days as of 4th quarter of 1398. While 13 Km road and 61 Rm bridges are delivered through 7 contracts during the reporting period.

2. JICA & GOA Fund

The project funded by JICA & GOV and the executing entity is NRAP-MoT. The cumulative budget of this project is almost US\$ 243 M in different years starting in SY1390 for delivering 621.66 Km of Asphalt roads and 2,120 Running meters of bridges in different provinces of Afghanistan. The design and procurement of this project completed.

Moreover, 82 contracts completed which through 438.83 Km road & 1,956 Rm bridges constructed and 2,720,708 number of labor days generated until quarter 4th of 1398. While 1.82 Km road is delivered through a single contract during the reporting period. Besides, construction of 93 Km road and 340 Rm bridges are positively in progress.

CHALLENGES AND OBSTACLE

1. Insecurity

Insecurity remained a serious challenge to the contract implementation. This challenge not only impose additional security measures which results in excessive money but also slow down the subproject progress, unregulated oversights, and negatively impact the workmanship quality.

To mitigate the risk on already awarded contract implementation, a third party and community-monitoring model implemented to reduce the contract cost and control workmanship quality; however, the concern still exists for upcoming new contracts.

2. Material Cost

The cost escalation of constructional substances critically affected the implementation trend. The basic estimation (Cost per Km) of secondary roads during ARAP project design was significantly low than the actual contractual cost per km, therefore the implementation pace is deadly slow particularly in case of asphaltting surfaces, however, to fill the financial gap additional finance requested and approved in 2017

3. Capacity of Private Sector

A detected major challenge in implementation was the lack of management capacity among national private companies. In response, program PIUs provide them training on regular interval to teach how to prepare bids and manage their working capital as well as implementation plans.

ANNEXES (A) MoT

Annex-A.1 Achievements During Reporting Period- 4th Quarter of 1398

Program-Ministry	Activity	Contracts Completed during Reporting Period						
		No. of Contracts	Road (KM)	Bridge (RM)	Structure (LM)	Structure Bridge	Labor Days	Contract Cost \$
NRAP-MoT	ARAP IDA+ARTF	3.00	26.09	0.00	6,842.00	6,842.00	38,019.69	2,534,646.00
	ARAP JICA/GOA	1.00	1.82	0.00	3,452.00	3,452.00	6,843.24	456,215.69
	ARAP PM	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	ARAP EM	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	ARAP PD	0.00	0.00	0.00	0.00	0.00	0.00	0.00
	ARAP RM	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total		4.00	27.91	0.00	10,294.00	10,294.00	44,862.93	2,990,861.69

Annex –A.2 Contracts at Different Stages of Implementation

Program-Ministry	Projects	Total no. of Contracts	Development			Procurement			Delivery		
			Completed	Ongoing	Planned	Completed	Ongoing	Planned	Completed	Ongoing	Cancelled/ Terminated
NRAP-MoT	LIWP-WB	312.00	312.00	-	-	312.00	-	-	300.00	-	-
	NEEP1-WB	217.00	217.00	-	-	217.00	-	-	209.00	-	-
	NEEPRA-WB	100.00	100.00	-	-	96.00	-	-	100.00	-	-
	NRAP-WB+DF	46.00	46.00	-	-	46.00	-	-	42.00	-	-
	NERAP-IDA+ARTF	140.00	140.00	-	-	140.00	-	-	137.00	-	-
	ARAP-IDA+ARTF	150.00	150.00	-	-	150.00	-	-	130.00	11.00	9.00
	ARAP- JICA/GOA	97.00	97.00	-	-	97.00	-	-	82.00	8.00	-
	ARAP-PM	22.00	22.00	-	-	22.00	-	-	23.00	-	-
	ARAP-RM-1,RM-2,RM-3, RM-4 & RM-5	507.00	507.00	-	-	507.00	-	-	507.00	-	5.00
	ARAP-EMR	34.00	34.00	-	-	34.00	-	-	34.00	-	-
	ARAP-PD	9.00	9.00	-	-	9.00	-	-	9.00	-	-
Total		1,634.00	1,634.00	-	-	1,630.00	-	-	1,573.00	19.00	14.00

Annex-A.3 Contracts Completed as of end of 4th Quarter 1398

Program-Ministry	Activity	Contracts Completed as of this Period						
		No. of Contracts	Road(KM)	Bridge(RM)	Structure(LM)	Structure Bridge	Labor Days	Contract Cost \$
NRAP-MoT	ARAP IDA+ARTF	130.00	997.12	1,489.10	135,672.00	137,161.10	2,528,070.39	159,667,603.59
	ARAP JICA/GOA	82.00	438.63	1,956.00	1,612.00	3,568.00	2,720,708.15	171,834,199.00
	ARAP PM	23.00	671.03	0.00	0.00	0.00	147,472.78	9,314,070.23
	ARAP-RM,RM2,RM3	507.00	5,537.00	0.00	0.00	0.00	108,934.46	6,880,071.23
	ARAP- PD	9.00	30.70	35.00	0.00	35.00	41,607.22	2,627,824.66
	ARAP EMR	34.00	178.44	0.00	0.00	0.00	41,607.22	2,627,824.66
Total		785.00	7,852.92	3,480.10	137,284.00	140,764.10	5,588,400.23	352,951,593.37

Annex- A.4 NRAP ongoing Projects during 4th Quarter 1398

Program-Ministry	Projects	Contracts Ongoing as of This Quarter						
		No. of Contracts	Road (KM)	Bridge (RM)	Structure(LM)	Structure Bridge	Labor Days	Contract Cost \$
ARAP-MoT	ARAP-IDA+ARTF	11.00	116.58	-	14,326.00	14,326.00	361,425.92	22,826,900.04
	ARAP JICA/GOA	8.00	93.00	340.00	8,746.00	9,086.00	529,812.62	33,461,849.93
	ARAP-PM	-	-	-	-	-	-	-
	ARAP-RM,RM2,RM3	-	-	-	-	-	-	-
	ARAP- PD	-	-	-	-	-	-	-
	ARAP-EMR	-	-	-	-	-	-	-
Total		19.00	209.58	340.00	23,072.00	23,412.00	891,238.54	56,288,749.97

Annex-A.5 NRAP MOT Achievements since inception to the end of 4th Quarter 1398

Program-Ministry	Projects	NRAP-MoT Overall Program Achievement Since Inception						
		No. of Contracts	Road Km	Bridge RM	Structures LM	Structure Bridge	Labor Days	Contract Cost \$
NRAP - MoT	LIWP-WB	312.00	3,897.96	3,436.50	24.00	3,460.50	3,403,984.00	12,223,000.00
	NEEP1-WB	217.00	2,200.90	644.50	22.20	666.70	2,591,107.00	10,714,000.00
	NEEPRA-WB	100.00	809.00	23,637.64	522.25	24,159.89	1,428,678.00	22,045,320.41
	NRAP-WB+DF	46.00	242.07	10,024.30	719.02	10,743.32	1,190,246.00	21,326,190.00
	NERAP-IDA+ARTF	137.00	1,122.88	54,777.10	1,521.50	56,298.60	1,753,698.18	140,600,000.00
	ARAP-IDA+ARTF	130.00	997.12	1,489.10	135,672.00	137,161.10	2,528,070.39	159,667,603.59
	ARAP-JICA/GOA	82.00	438.63	1,956.00	1,612.00	3,568.00	2,720,708.15	171,834,199.00
	ARAP-PM	23.00	671.03	-	-	-	147,472.78	9,314,070.23
	ARAP-RM (1,2,3)	507.00	5,537.00	-	-	-	108,934.46	6,880,071.23
	ARAP- PD	9.00	30.70	35.00	-	35.00	41,607.22	2,627,824.66
	ARAP-EMR	34.00	178.44	-	-	-	41,607.22	2,627,824.66
Overall Achievement		1,597.00	16,125.73	96,000.14	140,092.97	236,093.11	15,956,113.41	559,860,103.78

Annex- A.6 NRAP Donor Commitment

Program- Ministry	Donor	Projects	Commitment (USD)	Disbursement (USD)	Projects Status
NRAP - MOT	WB	LIWP	12,223,000.00	12,223,000.00	Completed
	WB	NEEP1	10,846,150.00	10,714,000.00	Completed
	WB	NEEPRA	21,755,279.00	22,045,320.41	Completed
	DFID	NRAP	21,326,190.00	21,326,190.00	Completed
	CIDA	NRAP	1,000,000.00	1,000,000.00	Completed
	SIDA	NRAP	521,385.60	521,385.60	Completed
	GOI	NERAP	3,021,074.21	3,021,074.21	Completed
	IDA+ARTF	NERAP	140,600,000.00	140,600,000.00	Completed
	IDA+ARTF	ARAP Road&Bridge	139,991,058.50	1,673,756.84	Completed
		NRAP JICA/GOA	154,753,134.50	9,490,143.66	Completed
		ARAP RM	6,880,071.23	-	Completed
		ARAP PM	9,314,070.23	640,367.47	Completed
		ARAP EM	2,627,824.66	-	Completed
		ARAP PD	2,627,824.66	-	Completed
		ARAP Road&Bridge	22,826,900.04	15,908,955.50	Ongoing
		NRAP JICA/GOA	53,532,739.28	18,723,847.94	Ongoing
		ARAP RM	-	-	Completed
		ARAP PM	-	-	Completed
		ARAP EM	-	-	
		ARAP PD	-	-	
Total			603,846,701.91	257,888,041.63	

Annex- A.7 ESM Reflection

Fourth Quarter 1398 Report		
No	Activity	Total
1	Number of ESM Plans Prepared	0
2	Number of Male Consulted	10
3	Number of Female Consulted	4
4	Number of Male trained	204
5	Number of Female trained	112
6	Number of Male (GRC) Established	0
7	Number of Female (GRC) Established	2
8	Number of PAFs	0
9	Number of Male PAPs	0
10	Number of Female PAPs	0
11	Land donated (m2) by people	0
12	Number of Trees Going to be Cut	0
13	Number of Trees Going to be Planted	0
15	Number of Stripe Plan Prepared	0
16	Number of Abbreviated RAP Prepared	0
17	Number of Projects Monitored/Visited	10
18	Number of Issues Solved	6

Ministry	Projects	Achievement During the Reporting Period
----------	----------	---

ANNEX (B) MRRD:

B.1 Achievements During The Reporting Period – 4th Quarter 1398

		No. of contracts Completed	Road (km)	Structures (linear meter)	Bridge (linear meter)	Total linear meter (Structure+Bridge)	Labor Days	Contract Cost (\$)
	ARAP-MRRD-WB	2	27	2,054	20	2,074	15,593	4,761,003
MRRD	NRAP - MRRD - MOF	7	13	3,595	61	3,656	28,460	1,929,278
	ARAP-MRRD-MoT	13	23	1,016		1,016	32,130	1,432,122
Total		22	63	6,665	81	6,746	76,183	8,122,403

B.2 CONTRACTS AT DIFFERENT STAGES OF IMPLEMENTATION

Ministry	Projects	No. of Contracts as per P.P	Development			Procurement			Delivery		
			Completed	Ongoing	Planned	Completed	Ongoing	Planned	Completed	Ongoing	Terminated
MRRD	MOF	-	811			620			492	118	1
	ARAP	402	557			448			402	42	5
Total		402	1,368	-	-	1,068	-	-	894	160	6

B3. CONTRACT COMPLETED FROM INCEPTION TO END OF 4th QUARTER 1398

Ministry	Projects	Works Budget In Million (\$)	Physical Target (km)	Completed Contracts						
				No. of Contracts completed	Road (km)	Structures (linear meter)	Bridge (linear meter)	Total linear meter (Structure+Bridge)	Labor Days	Contract Cost (\$)
MRRD	ARAP	80.5	379	402	1501.04	90614.17	2463.64	87,969.91	2,001,232	95,754,067.94
	MOF			492	1,719	243,687	3,299	246,986.74	2,323,466	155,392,620.71
	ARAP-MoT		443	14	25.04	1016			35,502	1,550,589.42
	Total	80.5	1429	908	3,245	335,318	5,763	334,957	4,360,200	252,697,278

B.4 CONTRACTS ONGOING DURING 4th QUARTER 1398

Ongoing Contracts							
Project	No. of Contracts	Road (km)	Structure s (linear meter)	Bridge (linear meter)	Total linear meter (Structure+Bridge)	Labor Days	Contract Cost (\$)
ARAP	42	63.15	13734.9	30	13,765	85,634	7813576.16
MOF	118	393	81,941	878	82,819	180,605	46,770,841
ARAP-MoT	50	60.4	9261			102915	5830389.46
Total	210	517	104,937	908	96,584	369,154	60,414,807

B.5 DONOR COMMITMENT FOR COMPLETED PROJECTS

Ministry	Donor	Project	Commitment In Million (\$)	Status of the Project
MRRD	MoF	MoF	201.8	Ongoing
	World Bank	ARAP	150	Ongoing
	Japan	Japan Fund	23.5	Completed
	DFID	CARD-F	1.52	Completed
	World Bank	NERAP	91.5	Completed
	APRP	APRP	15	Completed
	AusAID	URAP	11	Completed
	AusAID	RAD-TK	2.87	Completed
	JSDf	LIPWP	2	Completed
	World Bank	LIWP	3.24	Completed
	CNTF	CNTF1	5.29	Completed
	USAID	NEEPRA-US	14.74	Completed
	EC	NEEPEC	10.63	Completed
	JSDf	RAL	19.6	Completed
	PSIB	NEEPRA-PS	15	Completed
	World Bank	NEEP1	2.43	Completed
	World Bank	NEEPRA-WB	14.73	Completed
	World Bank	ILO	1.72	Completed
	World Bank	JPMU	2.29	Completed
	DFID	HARDP	16.25	Completed
CNTF	CNTF-LB	6	Completed	
Total			598.86	

B.6 NRAP OVERALL ACHIEVEMENTS SINCE INCEPTION

Ministry	Projects	Completed Contracts							
		Works Budget in m (\$)	# of Contracts completed	Road (KM)	Structure (RM)	Bridge (RM)	Total RM (Structure+Bridge)	Labor days	Contract Cost (\$)
NRAP-MRRD	HARDP - MRRD - DF	11.50	11,500,000	16	84	24	28	52	-
	NEEP1 - MRRD - WB	2.37	2,370,000	73	291	1,549	-	1,549	419,011
	NEEPEC - MRRD - EC	6.75	6,750,000	26	159	1,793	102	1,895	330,101
	NEEPRA - MRRD - AU	0.48	480,000	15	31	303		303	32,177
	NEEPRA - MRRD - CD	0.20	200,000	2	20	4		4	2,382
	NEEPRA - MRRD - DF	5.77	5,770,000	73	236	8,427	58	8,485	312,147
	NEEPRA - MRRD - PS	3.61	3,610,000	47	183	2,585	137	2,721	240,363
	NEEPRA - MRRD - US	1.51	1,510,000	4	58	636		636	11,604
	NEEPRA - MRRD - WB	8.33	8,330,000	248	708	8,928	117	9,045	1,300,885
	NERAP - MRRD - TF		-	134	428	11,418	383	11,801	456,860
	NERAP - MRRD - WB		-	279	920	20,273	1,219	21,492	1,404,919
	NRAP - MRRD - CF	3.99	3,990,000	4	46		162	162	22,642
	NRAP - MRRD - DU	0.70	700,000	4	16	319		319	6,415
	RAD-TK -AU	1.91	1,910,000	16	24	250	45	295	104,935
	NRAP-LB - MRRD - CF	5.02	5,020,000	96	143	3,941		3,941	578,382
	RAL - MRRD - JF	9.42	9,420,000	34	349	9,506	10	9,515	359,800
	APRP-NRAP-MRRD	15.00	15,000,000	29	86	4,104		4,104	482,684
	CARD-F			3	13	6,777		1,293	22,365
	URAP			39	52	496		496	114,455
Total	76.56		1,142	3,847	81,332	2,260	78,108	6,202,128	

B.7 ESM Reflection

Details of ESM activities during the reporting period											
S/no	Activity	Kabul	West	CHL	East	North	South East	South	North East	Badakhs han	Total
1	# of ESM documents prepared	6	0	2	0	1	2	1	1	1	14
2	# of trees planted	0	0	150	120	0	400	0	0	200	870
3	# of people awareness and trained	730	220 M 120 FM	96 M 10 FM	85	270	719	40	0	15	2175 M 130 FM
4	# of coordination meetings held	15	3	3	5	3	3	8	1	0	41 M 0 FM
5	# of GRC established	9	2 M 5 FM	3 M 1 FM	3	1	8 M 8 FF	5 M 2 FM	0	1	32 M 16 FM
6	# of issues solved	0	0	0	1	1	1	0	0	0	3
7	# of CPM conducted	1	4	0	9	6	4	4	0	0	28 M 0 FM
8	# of Social Audits conducted	0	0	0	0	0	0	0	0	0	0
9	Land donated (m2)	4844	0	0	2250	0	4350	2000	0	1150	14594
10	Environmental Monitoring	0	0	0	9	0	4	0	0	12	25 M 0 FM

*M (Male GRC)

*FM (Female GRC)

* PM (Periodic Maintenance)

B.8 Financial Status of other Ongoing Projects

B.8.1. MoF Financial Details

MoF 1399 FY						
Component	Budget	Disbursement			Balance	%
		Till previous	This period	To date		
Works	32,573,320	-	530,056	530,056	32,043,264	2%
Non Works	2,881,226	-	147,494	147,494	2,733,732	5%
Total	35,454,545	-	677,549	677,549	34,776,997	2%
